

Project: Still Branch WTP AFD and Date: Thu 6/27/24

Task: Still Branch WTP AFD and Date: Thu 6/27/24

Task Mode: Task, Split, Milestone

Summary: Summary, External Milestone, Inactive Milestone, Inactive Task, Inactive Milestone

Project Summary: Project Summary, External Task, Inactive Task, Inactive Milestone

External Tasks: External Tasks, External Milestone, Inactive Milestone

Manual Summary: Manual Summary, Manual Task, Duration-only

Manual Summary Rollup: Manual Summary Rollup, Manual Summary, Start only

Finish-only: Finish-only, Deadline, Critical


Critical Split: Critical Split, Baseline, Baseline Milestone

Baseline Summary: Baseline Summary, Progress, Baseline Milestone

Legend:

- Task
- Split
- Milestone
- Summary
- External Milestone
- Inactive Milestone
- Inactive Task
- Inactive Milestone
- Project Summary
- External Task
- Inactive Task
- Inactive Milestone
- Manual Summary
- Manual Task
- Duration-only
- Manual Summary Rollup
- Manual Summary
- Start only
- Finish-only
- Deadline
- Critical
- Critical Split
- Baseline
- Baseline Milestone
- Baseline Summary
- Progress
- Baseline Milestone

ID	Task Name	Task Mode	Duration	Start	Finish	Predecessor	August	September	October	November	December	January	February	March	April	May	June	July	August	September	October	November	December
97	Plant Instrumentation	Task	5 days	Fri 1/10/25	Thu 1/16/25	96	7/28 8:5	8/13/25	8/27/25	9/10/25	9/23/25	10/7/25	10/20/25	10/31/25	11/10/25	11/23/25	12/7/25	12/20/25	1/3/26	1/16/26	1/29/26	2/12/26	2/26/26
98	EQUIPMENT INSTALLATIONS	Task	10 days	Fri 1/17/25	Thu 1/30/25	97																	
99	Install Screen/Headworks Bypass Structure	Task	2 days	Fri 1/17/25	Mon 1/20/25	97																	
100	Install Filter	Task	1 day	Tue 1/21/25	Tue 1/21/25	99																	
101	Install UV Module	Task	1 day	Wed 1/22/25	Wed 1/22/25	100																	
102	Install Blowers	Task	1 day	Thu 1/23/25	Thu 1/23/25	101																	
103	Piping Connections to Equipment	Task	5 days	Fri 1/24/25	Thu 1/30/25	102																	
104	PAINTING	Task	5 days	Fri 1/31/25	Thu 2/6/25	103																	
105	Paint Piping	Task	5 days	Fri 1/31/25	Thu 2/6/25	103																	
106	FINAL SITEWORK	Task	15 days	Fri 2/7/25	Thu 2/27/25	105																	
107	Final Site Cut and Shift	Task	5 days	Fri 2/7/25	Thu 2/13/25	105																	
108	Gravel Paving	Task	5 days	Fri 2/14/25	Thu 2/20/25	107																	
109	Grassing	Task	5 days	Fri 2/21/25	Thu 2/27/25	108																	
110	STARTUP PLANT	Task	5 days	Tue 9/30/25	Mon 10/6/25	8																	
111	SUBSTANTIAL COMPLETION	Task	1 day	Tue 10/7/25	Tue 10/7/25	110																	
112	PUNCH LIST	Task	10 days	Wed 10/8/25	Tue 10/21/25	111																	

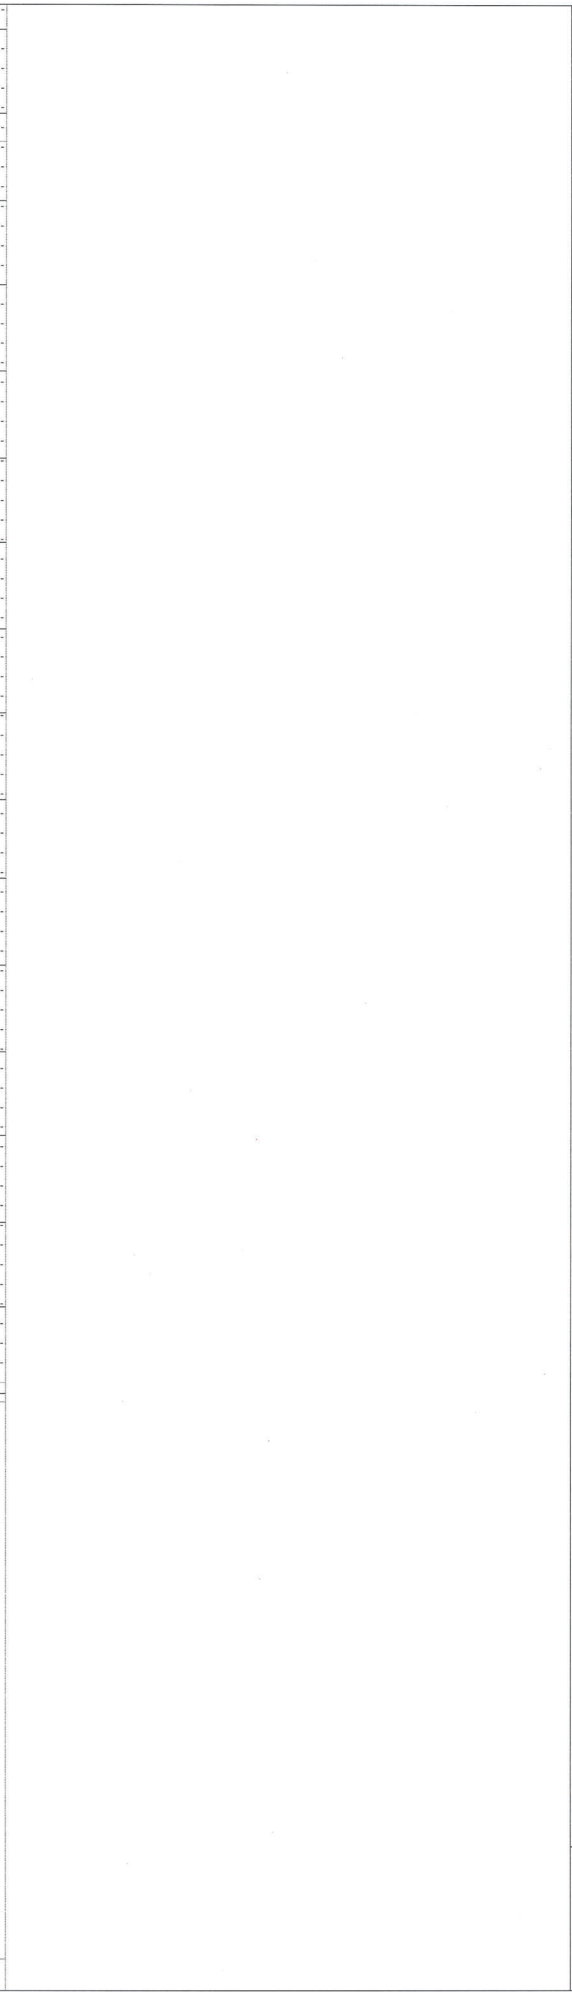

Project: Still Branch WTP AFD and Split
Date: Thu 6/27/24

Task: Task, Milestone, Split

Summary: Summary, Project Summary, External Tasks

External Milestone: External Milestone, Inactive Task, Inactive Milestone

Inactive Summary: Inactive Summary, Manual Task, Duration-only

Manual Summary Rollup: Manual Summary, Start-only

Task-only: Task-only, Manual Summary, Start-only

Baseline Summary: Baseline Summary, Progress

Critical Split: Critical Split, Baseline, Milestone

Legend:

- Task: Solid blue bar
- Milestone: Dotted blue bar
- Split: Dashed blue bar
- Summary: Solid blue bar
- Project Summary: Dotted blue bar
- External Tasks: Solid blue bar
- External Milestone: Dotted blue bar
- Inactive Task: Dashed blue bar
- Inactive Milestone: Dotted blue bar
- Manual Task: Solid blue bar
- Duration-only: Dotted blue bar
- Manual Summary: Solid blue bar
- Start-only: Dotted blue bar
- Baseline Summary: Solid blue bar
- Progress: Dotted blue bar
- Critical Split: Dashed blue bar
- Baseline: Solid blue bar
- Milestone: Dotted blue bar

NORTH LIMESTONE COUNTY WRF
